

CCS2002 | CSE2002 - Group Project

Progress Report 1

Project Identification Information

Project title	: Centralized E-Commerce Platform for laptop sales and Auction Management System
Student names with initials and Index Numbers	: M.A.O. Rodrigo – FC221019 : U.J.N.S. Tharaka – FC222050 : S. Gunaruban – FC222041 : D.P. Gamage – FC221033 : U.S. Ravihara – FC222028 : U.K.D.S. Sandaruwan – FC221006 : L.R. Thuduwege – FC222002 : K.G.A.K. Sathsarani – FC222015
Supervisor's name	: Mr. K. D. T. Rangana

Progress Report Period

Start Date: 29-05-2025

End Date: 06-11-2025

Work Carried out between this meeting and previous meeting

- **Created Project Proposal**

With assistance of Full-Stack developer, Project Manager engaged in the creation of the Proposal of this project. All functional and non-functional requirements were identified, and the proposal was created accordingly.

- **Requirement gathering phase**

This phase was successfully completed by the Analyst with the collaboration of the Designer. This phase involved identifying and analysing already existing systems that are similar to our proposed system. Total of 10 existing systems were reviewed by the Analyst and the Designer, however only 5 systems were analysed thoroughly with in detail analysis. These insights gave us a proper understanding into our proposed system and its behaviour.

- **Design phase initiation**

After the completion of Requirement gathering phase, design phase was initiated. It started with the development of UML diagrams. This work was mainly carried out by the Designer with the help of Full-stack developer and Project Manager.

- **UML and Database design**

Use case diagrams: Developed for both existing and proposed system to show the user interactions and system functionalities.

Class diagram: Class diagram for the proposed system was developed.

Activity diagram: Three activity diagrams were prepared to represent the major workflows within the system.

Entity Relationship diagram: The initial design of the database was constructed in the form of an ERD.

Evidence of Work Carried out between this meeting and previous meeting




Meeting taken on 29-05-2025




Meeting taken on 03-06-2025



Meeting taken on 24-06-2025

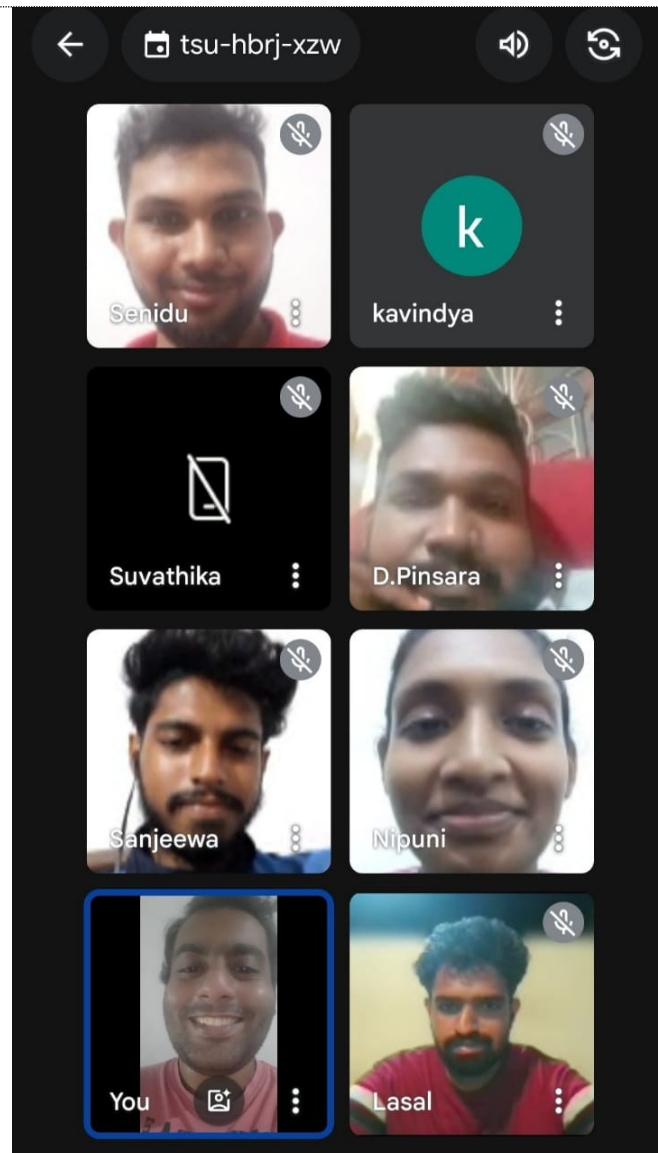

Online meeting taken on 02-11-2025



Designs made up to now

<u>Problems Encountered</u>
• Identification of Attributes for ERD
It was challenging to identify and finalize all the necessary attributes for the Entity-Relationship Diagram (ERD) prior to development. Some entities required revisions after further analysis of system requirements.
• Change in Technology Stack
Due to technical feasibility and compatibility issues, the initial plan to use Firebase for Backend-as-a-Service (BaaS) was revised. The team decided to switch to Supabase , which offered better alignment with the project's database and API requirements.
• Complexity in Designing UML Diagrams
Developing complete and accurate UML diagrams proved to be time-consuming and complex. Ensuring consistency across multiple diagrams (Use Case, Class, and Activity) required several iterations and team discussions.
• Coordination delays
Various work and scheduling issues caused conflicts in meeting times for team members which delayed some meetings.
<u>Planned work that were unable to carry out with reasons</u>
• Incomplete Design Stage
The design phase could not be fully completed as initially planned. Additional time was required to refine the existing UML diagrams and finalize the Entity-Relationship Diagram (ERD). The team prioritized accuracy and consistency in design artifacts, which led to a delay in completing the remaining components of the design stage.
• Pending UML Diagrams
The UML Sequence , State , Component , and Deployment diagrams were not completed during this period. This was primarily due to the extended time spent on requirement validation and on ensuring the correctness of the initial UML diagrams (Use Case, Class, and Activity). The initial plan was to complete these design diagrams early, but upon further discussion with teammates and consultation with Supervisor, we decided to hold the design of these diagrams for now and focus on making the initial diagrams more accurate.

Work planned until next meeting		
Design completion planned alongside development The team aims to finalize the design phase by completing all remaining UML diagrams, including the Sequence, State, Component, and Deployment diagrams concurrently with the development stage. This will ensure a comprehensive representation of the system's structure and behaviour. We are planning on making these diagrams during the development stage as we can make the necessary changes to the diagrams with the development and rectify any issues.		
Revision of Existing Design Diagrams Any necessary modifications or updates to the current design diagrams will be carried out to reflect changes identified during the development process or feedback from supervisors and team reviews.		
Commencement of the Development Stage The team plans to initiate the development phase of the project. This will involve setting up the development environment, configuring the chosen backend service (Supabase), and beginning implementation of core system modules. These tasks will be carried out by the Front-end developer, Back-end developer and the Full-stack developer		
Meeting information		
Meeting Date: 02-11-2025		
Meeting time	Start: 8.00 P.M	End: 10.00 P.M
Number of participants: 8		
Supervisor's Comments		
Student has done	☐ More than enough ☐ Sufficient ☐ Not Enough ☐ No	work.
Student is progressing	☐ Well ☐ Sufficiently ☐ Not Enough	In the project.

Further Comments (if any)		
Student's Signature		Supervisor's Signature
